







Scope of Work

The drilling of shoring caisson piles is scheduled to be completed in mid-December. Once complete, the drill will be demobilized. The installation of dewatering components will continue at various locations on site. Towards the end of the month, bulk excavation will commence on the south side, to the level of the first row of tiebacks.

What to Expect



- Drilling activity on-site shoring and tieback installation.
- · Excavation activity on south side.



- Truck traffic at gate #2 (Yorkville Avenue)
- · Potential traffic disruptions.



· General noise, vibrations, dust and debris.



• Temporary closure of curb lane on Avenue Rd to accommodate our covered walkway.

(See Figure 4 on page 2).



(Figure 2): Site progress of NW corner, view of a concrete truck.



(Figure 3): View of the shoring drill working across the north elevation.

Project

138 Yorkville Avenue **Mixed-Use Development**

Project Stage

Shoring, Excavation and **Tieback Drilling**

Projected Timeline for Shoring Activities

March 2023 - December 2023

Work Hours

Monday to Friday 7:00a.m to 7:00p.m

Contact Us


Emergency Contact Line (416) 849-1523

General Inquiries info@138 york villeupdates.ca

Website

www.138yorkvilleupdates.ca



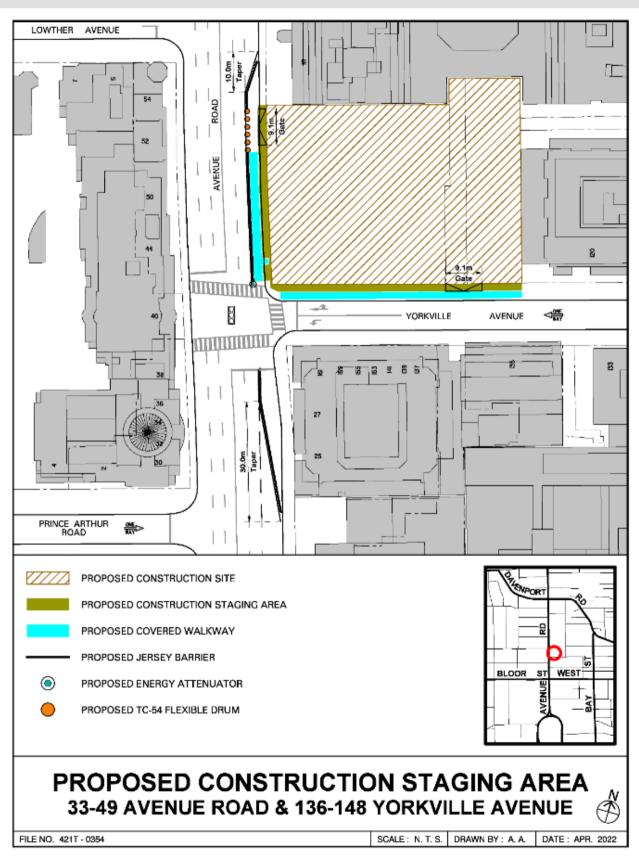

(Figure 4): Construction Staging Area
